Act ID	Description	Orig Dur	Pred	Succ
Project Milestones				
1010	Contract Date	0		1080, 2310
1080	Construction Start	0	1010	2310
1060	Footing Placement	0	3040	
1110	Pylon Sign Base Complete	0	2230	
1120	Building Dry	0	3180	
1130	Walk In Cooler Install	0	4040	
1030	Substantial Completion	0	2010, 2110,	
1050	Final Completion	0	4230	
Sitework				
2310	Erosion Control	1	1010, 1080	2180, 2300
2180	Relocate Existing Utilities	5	2310	2330
2300	Site Grading	5	2310	2030, 2040,
2190	Underground Storm Sewer	5	2300	2040, 2070,
2200	Underground Sanitary Sewer	5	2300	2040, 2080,
2280	Webcam Pole	5	2300	2060
2080	Underground Gas	2	2190, 2200,	2030
2090	Underground Fire Sprinkler	2	2190, 2200,	4080
2100	Underground Water	2	2190, 2200,	2030
2040	Underground Telephone / Data	5	2190, 2200,	2030, 2330
2070	Underground Electrical Primary	5	2190, 2300	2030, 2060,
2060	Transformer Pad	2	2070, 2280	2050
2330	Fine Grade	2	2040, 2070,	2030
2050	Set Transformer	1	2060	2320
2030	Curb & Gutter	3	2040, 2070,	2010, 2130,
2210	Pipe Bollards	2	2030	2160, 3240
2130	Dense Grade Base	5	2030	2140, 2150
2240	Light Pole Bases	5	2030	2250
2010	Traffic Signalization	20	2030	1030
2230	Pylon Sign Base	25	2030	1110
2140	Asphalt Binder	2	2130	2150, 2220,
2250	Light Poles	2	2240	2220
2160	Concrete Paving	5	2030, 2210,	2120, 2220,
2170	Concrete Sidewalks	5	2030, 3200	2220, 2320,
2290	Wood Fence	5	2160	3240
2320	Irrigation	5	2050, 2140,	2220
2220	Landscaping	5	2140, 2160,	2150
2150	Asphalt Seal Coat	1	2130, 2140,	2110, 2120,
2120	Traffic Signage	1	2150, 2160	1030
2260	Flexible Delineator Posts	1	2150, 2160	1030
2270	Concrete Wheel Stops	1	2150, 2160	1030
2110	Striping	2	2150, 3210	1030

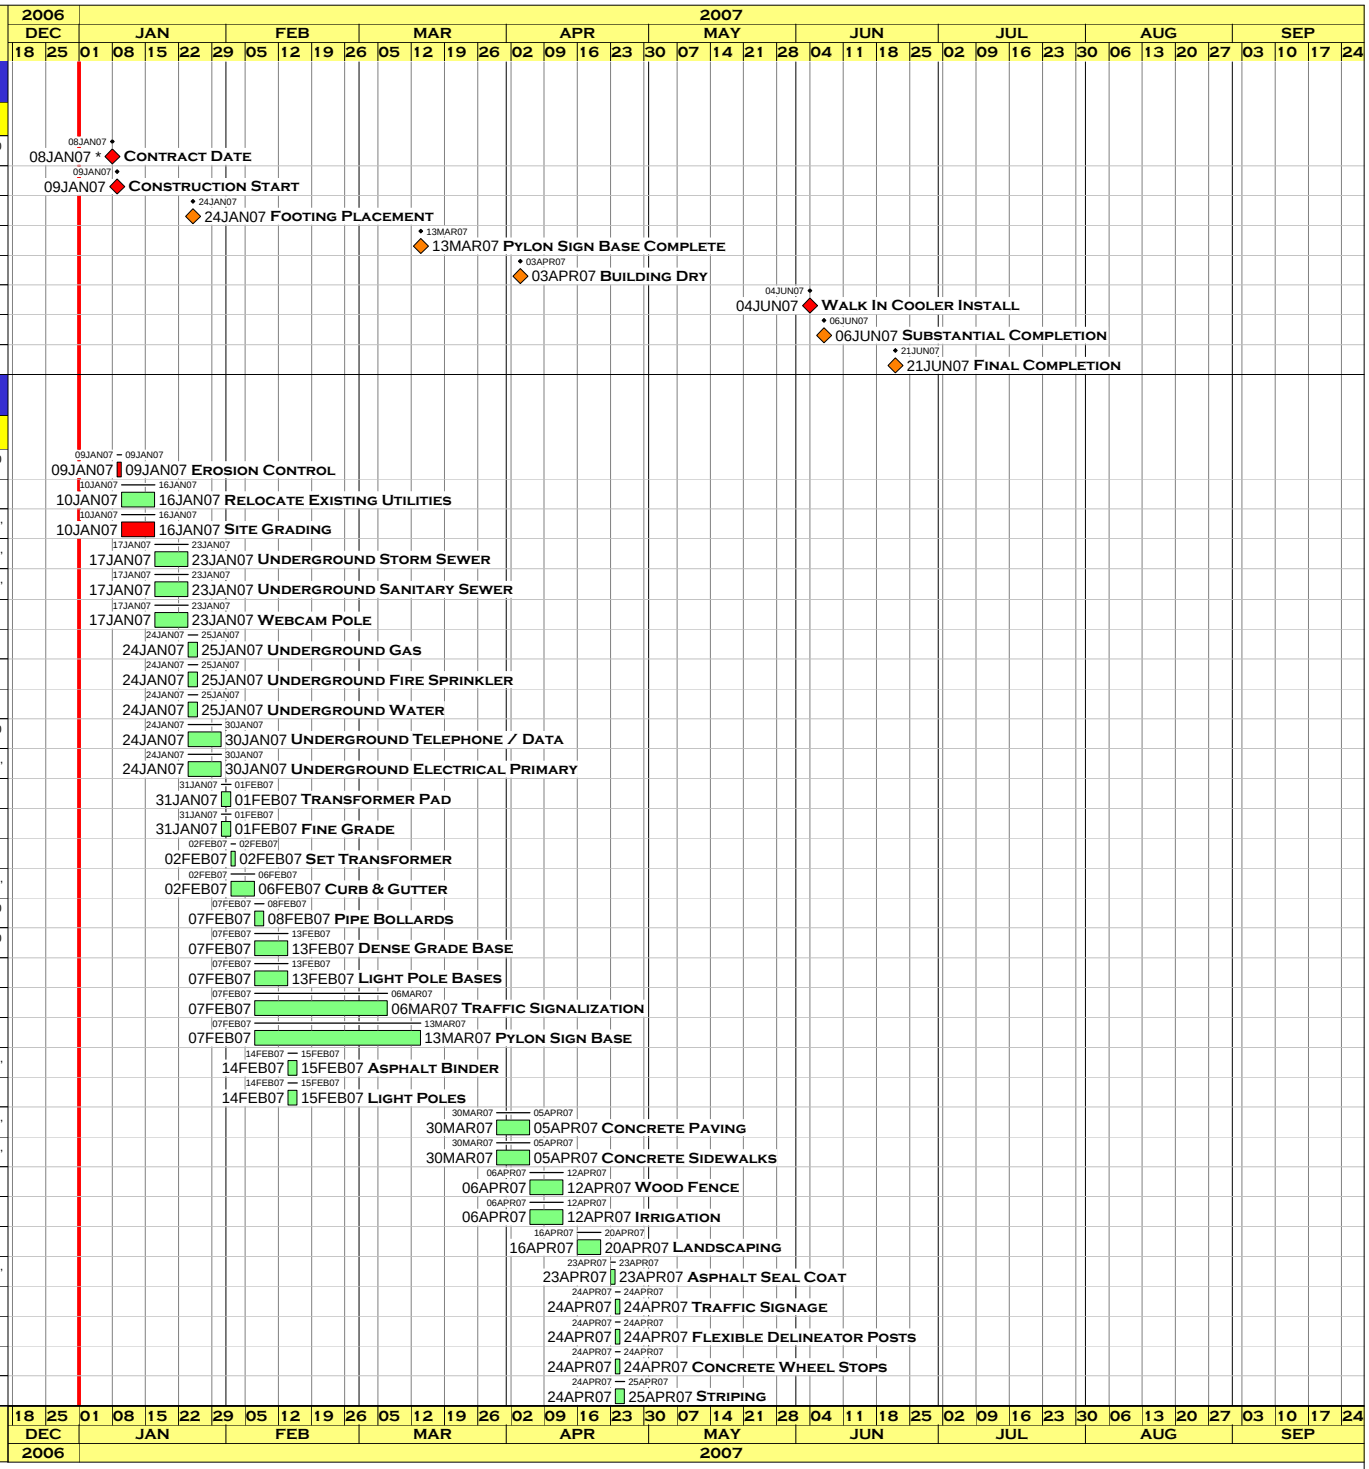

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

WSS02 (SureTrak)
Report: WG1
Layout: 11x17
Filter: All Activities

Job Name
Company Name

Run Date: 28SEP07
Data Date: 01JAN07
Job# Input Job Number

WSS
Wolnski Scheduling Services, Inc.

Act ID	Description	Orig Dur	Pred	Succ
Building Shell				
3040	Footings - dig, reinforce, pour	6	2300	1060, 3080,
3100	Underslab Fire Sprinkler	2	3040	3120
3110	Underslab Gas	2	3040	3120
3080	Underslab Plumbing	4	3040	3090
3090	Underslab Electrical	2	3040, 3080	3120
3120	Prep & Pour Slab On Grade	5	3040, 3090,	3050, 3220
3220	Exterior HM Frames	1	3120	3230
3050	Exterior CMU	10	3120	3060, 3200
3060	Structural Steel	10	3050	3070, 3200
3070	Metal Deck	5	3060	3180, 3190,
3200	Masonry Veneer	15	3050, 3060	2160, 2170,
3190	Wood Blocking	3	3070	3140, 3180
3180	Roofing	10	3070, 3190	1120, 3130,
3230	Exterior HM Doors	1	3200, 3220	3240
3250	Receiving Door	1	3200	3240
3160	Exterior Light Fixtures	3	3200	1030
3290	Metal Stud Trusses (Canopy)	3	3200	3240, 3300
3150	Tube Steel Awning	5	3200	3240
3170	Aluminum Storefront	5	3200	4090
3130	Set HVAC Units	1	3180	4380
3340	Roof Hatch	1	3180	4090
3140	Metal Coping	3	3180, 3190	3240
3300	Plywood Decking (Canopy)	3	3290	3210, 3260
3020	Scuppers & Downspouts	3	2170, 3200	2220
3280	Drive Thru Window Assembly	3	2160, 3200	4090
3210	Standing Seam Metal Roof (Canopy)	5	3300	2110, 2220,
3260	Vertical Flush Metal Panels	5	3300	2150
3240	Exterior Paint	5	2210, 2290,	3270
3270	Exterior Signage	2	3200, 3240,	1030
Interior Finishes				
4280	HM Frames	1	4020	4270
4020	Metal Stud Framing/Furring	5	3070	4050, 4060,
4060	Plumbing Wall/Overhead Rough In	5	3070, 4020	4100
4050	Electrical Wall/Overhead Rough In	10	3070, 4020	3270, 4070,
4350	Wood Blocking	5	4020	4090
4070	Mechanical Overhead Rough In	10	3070, 4020,	4100, 4380
4080	Fire Sprinkler Overhead Rough in	10	2090, 3070,	4100
4100	Framing Inspection	0	4020, 4050,	4090, 4340
4340	Insulation	1	4100	4090
4380	HVAC Connections / Start Up	5	3130, 4070	4220
4090	Hang & Finish Sheetrock Walls & Ceilings	8	3170, 3180,	4110, 4170,
4220	Conditioned Air	0	4380	4370

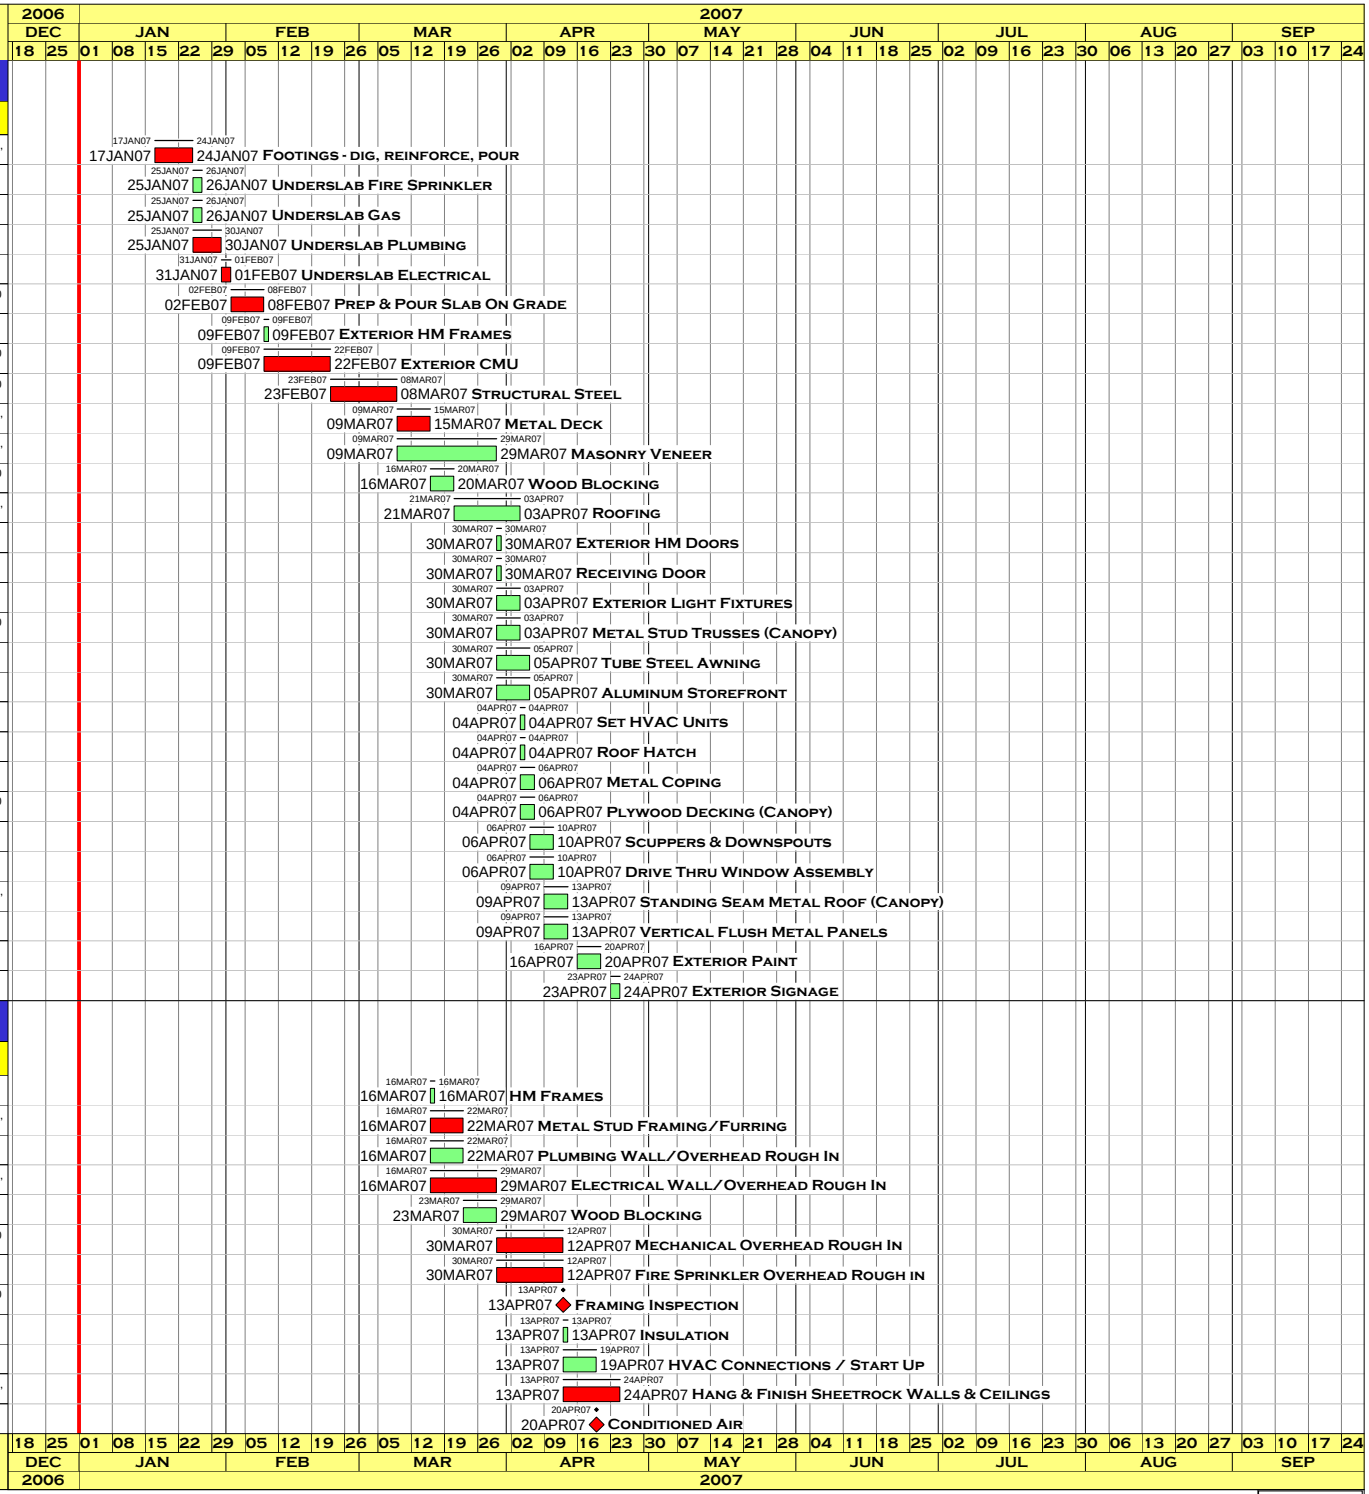

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

WSS02 (SureTrak)
Report: WG1
Layout: 11x17
Filter: All Activities

Job Name
Company Name

Run Date: 28SEP07
Data Date: 01JAN07
Job# Input Job Number

WSS
Wolnski Scheduling Services, Inc.

Act ID	Description	Orig Dur	Pred	Succ
4170	Prime & First Coat Paint	5	4090	4110, 4200,
4180	Ceramic Tile	5	4090	4320, 4360
4110	Ceiling Grid	4	4090, 4170	4030, 4120,
4370	Millwork / Countertops	4	4090, 4110,	4200, 4210,
4120	Electrical Trim Out	5	4110	4030, 4160,
4140	Mechanical Trim Out	5	4110	4030, 4160,
4150	Fire Sprinkler Trim Out	5	4110	4030, 4160,
4300	Slatwall	5	4110, 4170	4030
4320	Fiberglass Wall Paneling	5	4110, 4170,	4360
4310	Masonite Wainscot	3	4110, 4170,	4250
4330	Vinyl Wallcovering	4	4110, 4170,	4190
4200	Carpet	5	4110, 4170,	4270
4260	Overhead Inspection	0	4120, 4140,	4160
4160	Ceiling Tile	3	4120, 4140,	4030, 4210,
4210	Rubber Flooring	3	4110, 4160,	4190
4250	Finish Paint	3	4160, 4310	4290, 4360,
4030	VCT	5	4110, 4120,	4040, 4130,
4290	Corner Guard	1	4250	4190
4440	Bath Acessories	2	4250	4230
4360	Toilet Partitions	4	4110, 4180,	4130, 4230
4270	Wood Doors & Hardware	2	4020, 4030,	4190
4040	Walk In Cooler	5	4030	1130, 4190,
4130	Plumbing Fixtures	2	4030, 4360	4190
4190	Final Clean	3	4040, 4130,	1030, 4230
4230	Punch List/Corrections	11	4040, 4190,	1050

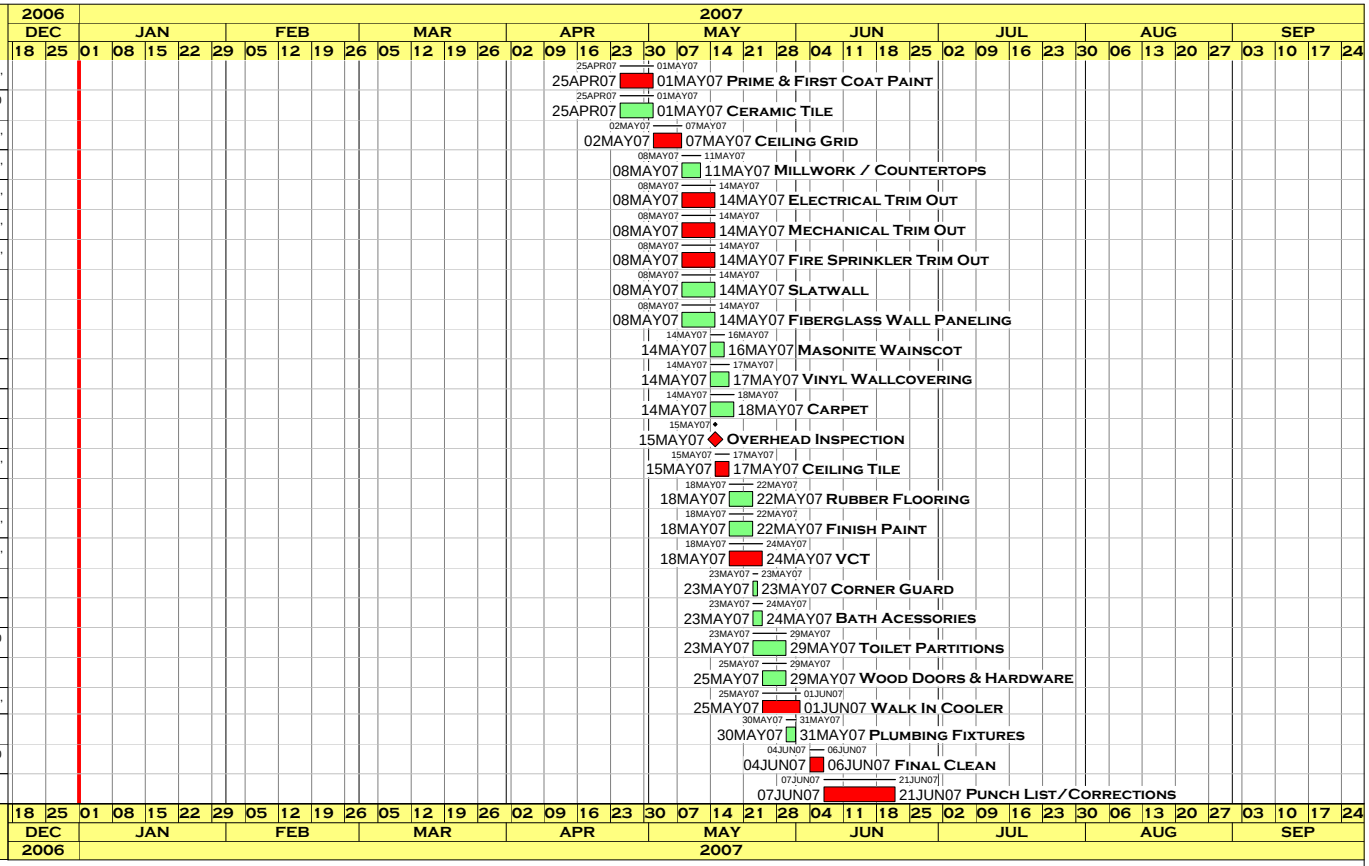

Early bar
Target bar
Progress bar
Critical bar
Start milestone point
Finish milestone point

WSS02 (SureTrak)
Report: WG1
Layout: 11x17
Filter: All Activities

Job Name
Company Name

Run Date: 28SEP07
Data Date: 01JAN07
Job# Input Job Number

WSS
Wolnski Scheduling Services, Inc.
